Task#	Description	Start Date	End Date	Duration in Days			Effort Hours Estimate	Effort Hours Complete	Effort Hours Left	Input	Output	Responsible	Status
001	Project Start and End Dates	2/8/2024	4/18/2024	70									
002	Project Proposal Rough Draft	2/9/2024	2/12/2024	3			2	2	0	Project requirements, Directions	Proposal draft	All	Complete
002	First Status Report	2/9/2024	2/12/2024	3			1	1	0	Project requirements, Directions	Status update report	Alexander Schoolcraft	Complete
003	Project Proposal Pitch Meeting	2/12/2024	2/12/2024	0			0.5	0.5	0	Proposal, status update	Meeting with "client"	All	Complete
004	Project Proposal Submission	2/12/2024	2/16/2024	4			4	4	0	Pitch meeting, rough draft	Final project proposal	Benjamin King	Complete
005	Develop User Stories	2/13/2024	2/19/2024	6			8	8	0	Proposal, plans	User Stories	All	Complete
006	Stakeholder Analysis	2/13/2024	2/19/2024	6			2	2	0	Project requirements	Stakeholder Report	All	Complete
007	Define Scope Boundries	2/12/2024	2/13/2024	1			0.5	0.5	0	Project requirements	Scope	All	Complete
008	User Story Refinement	2/19/2024	2/26/2024	7			8	8	0	User Stories	Backlog, Sprints built	All	Complete
009	High-Level Archetecture Design	2/26/2024	2/29/2024	3			2	2	0	Project requirements	Architecture design	All	Complete
010	GUI design sketch	2/26/2024	2/29/2024	3			8	8	0	Architecture design	GUI interface	Alexander Schoolcraft	Complete
011	Sprint Planning	2/29/2024	3/4/2024	4			8	8	0	Architecture design, user stories	Forward plans	All	Complete
012	Development Cycles - Plan/Build/Test	3/4/2024	4/22/2024	49			0	0	0	Sprints, requirements, backlog	Project coded	All	Complete
12a	Sprint 1: Login Page	3/4/2024	3/11/2024	7			8	8	0		Log-In page running	All	Complete
12b	Sprint 2: Main Landing Splash	3/11/2024	3/18/2024	7			8	8	0		Landing page running		Complete
12c	Sprint 3: Build Lists/Webview	3/18/2024	3/25/2024	7			8	8	0		Webview page running		Complete
12d	Sprint 4: List View page	3/25/2024	4/1/2024	7			8	8	0		List View Page running		Complete
12e	Sprint 5: Purchase options page	4/1/2024	4/8/2024	7			8	8	0		Purchase options page running		Complete
12f	Sprint 6: Securing the System	4/8/2024	4/15/2024	7			8	8	0		Security features in place		Complete
12g	Sprint 7: Full System Testing	4/15/2024	4/18/2024	3			8	8	0		System tested and fully operational		Complete
13	Documentation	4/18/2024	4/23/2024	5			20	20	0	Product	User Manual, Tools Used, etc		Complete
14	Presentation and Handoff	4/26/2024	4/26/2024	0			1		1				Not Started
				0					0				
				0					0				
				0					0				
				0					0				
				0					0				
				0					0				
				0					0				
				0					0				
				0					0				
				0					0				
				0					0				
				0					0				
				0					0				
				0					0				
				0					0				
				0					0				
				0					0				
				0					0				
				0					0				
				0					0				
				0					0				
				0					0				
				0					0				
				0					0				
				0					0				
				0					0				
				0					0				
				0					0				
				0					0				
				0					0				

CALENDAR DAYS PASSED AND LEFT
Days Left, -832, -
48%
Days Passed,
902, 52%

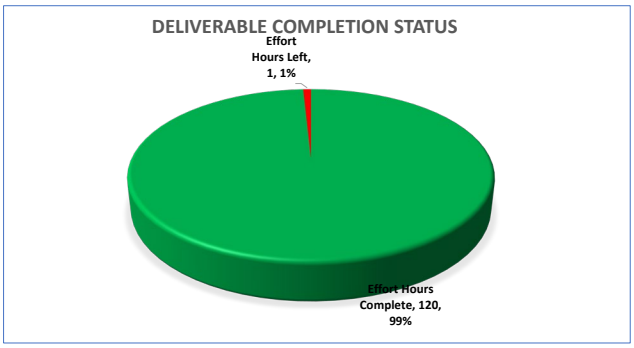
DELIVERABLE COMPLETION STATUS
Effort
Hours Left,
1, 1%
Effort Hours
Complete, 120,
99%
